AMTCS DEPLOYMENT INTEGRATION SUPPORT & ASM DEVELOPMENT STATUS

Gary Grote

NAVSEA

Keyport

June 27, 2000

Electronic Classrooms (ECR) Deployment

NAS Whidbey Is.

- 16 ECR installed (May-Jun 00)
- Networked 2 additional ECR (Jun 00)
- Backordered graphics tablets received and being installed

Electronic Classrooms (ECR) Deployment

NAS North Is.

- 7 ECR Installation in progress
  - 75% complete (as of 6/26)
  - Estimated completion - 6/30
- Backordered graphics tablets being received and installed

Electronic Classrooms (ECR) Deployment

- Others:
  - Staging and Shipping continue as scheduled for all other sites

Planned FY00 ECR Deployments

Task Name	3rd Quarter			4th Quarter			1st Qua	
	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
Schoolhouse								
Whidbe- 4 AECs, 6 IECs, 1 LRC, Integrate Networ 2 AECs (CNET- 3	4			6/26				
North Islanc- 3 AECs (CNE- 2 AECs, 2 IECs)		5/26		6/30				
New Bern- Upgrad 1 IEC to LRC			6/22	7/14				
Cherry Point- 1 AEC (CNE- 1 AEC)			6/20	7/20				
McCutcheo- (CNE- 1 LRC)			6/26	7/24				
New River- (CNE- 1 LRC)			6/26	7/25				
Mirimar- (CNE- 1 LRC)			7/3	8/8				
Camp Pendelto- (CNE- 1 LRC)			7/3	8/15				
Jacksonvill- 4 AECs, 5 IECs, Integrate/ Networ 2 AECs (CNE- 2 AECs, 2 IECs)			6/19	8/25				
Tinker- 3 AECs, 3 IECs (CNE- 1 IEC)				7/7	9/8			
Pt. Mugu- 3 AECs, 3 IECs, 1 LRC				7/21	10/5			
Maypor- 3 AECs, 3 IECs, Add develope station to LRC & Integrate				8/4	10/6			

Fleet Training Devices (FTD) Deployment

- Installation of 7 FTD Suites with ASM Ver. 1.1 in support of 90 day trial
  - VF2, VF101, VFA 106 Installations and Training are complete
  - Remaining Materials have been shipped to sites

FTD Deployment

- FTD Standalone (Courseware Only)
  - Deployed 16 of 96 E2/C2 courseware only
  - Plan to complete E2/C2 Deployments by 22 July

FTD Deployment

- 18 additional FTDs provided to support courseware development, Training Effectiveness Evaluation and TYCOM working groups

Planned FY00 FTD Deployments

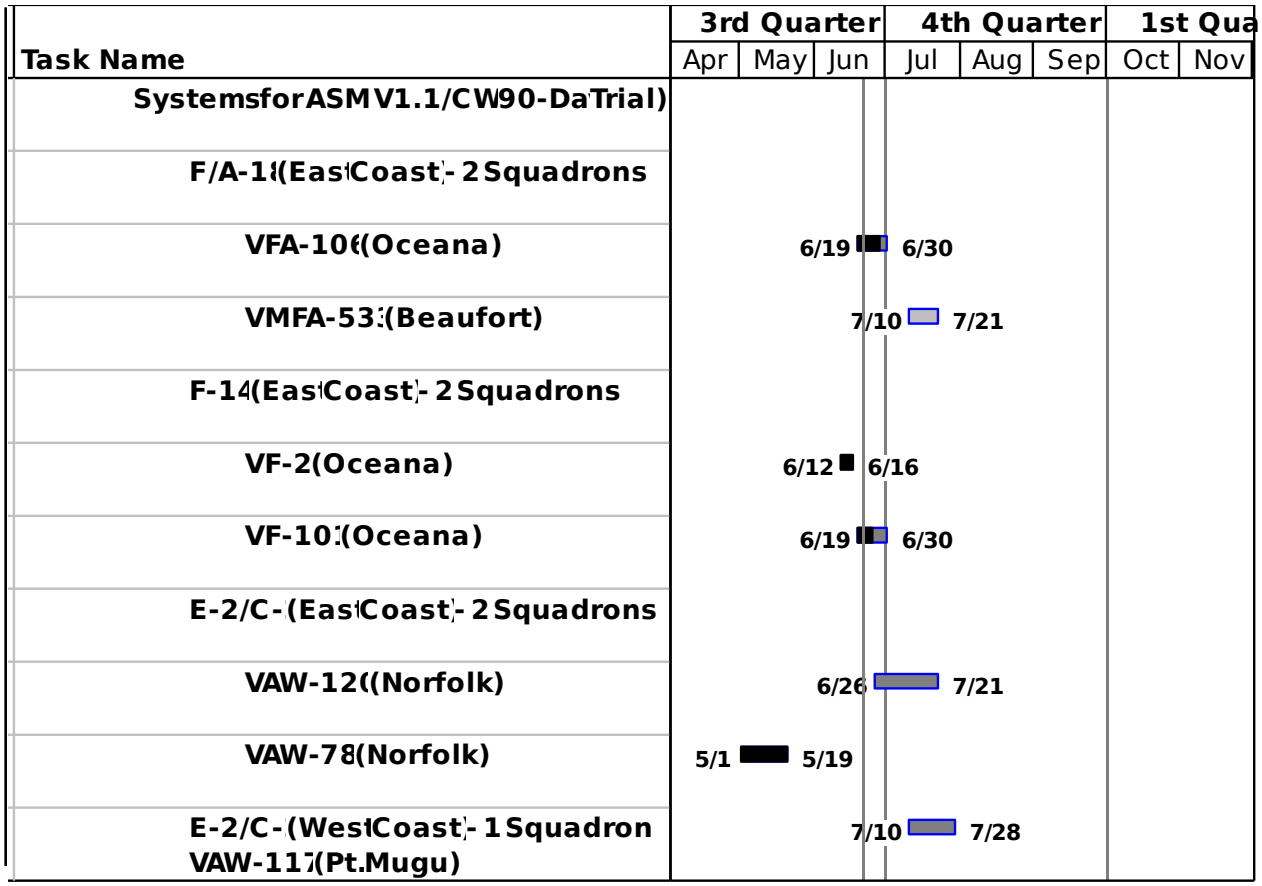

Planned FY00 FTD Deployments

Task Name	3rd Quarter May	3rd Quarter Jun	4th Quarter Jul	4th Quarter Aug	4th Quarter Sep	1st Qua Oct	1st Qua Nov
SystemswithCoursewareOnly							
E2/C2(CoursewareOnly) - 96 Laptops							
Shipping		6/2					
F/A-18(CoursewareOnly) - 194 Laptops							
Shipping			7/3				
H-60(CoursewareOnly) - 202 Laptops2 Desktops							
Shipping					9/8		
E-6A/B(CoursewareOnly) - 17 Laptops							
Shipping						10/6	

FTD Issues

- ICW Deliveries
  - F/A18 ICW Delivery date slipping to the right
    - Need firm dates to set schedule

- Batteries for Dual Laptops
  - Failing on the shelf
  - 315 batteries are required
  - Batteries on order

Integration

Courseware

- E2/C2 integrated
- AV-8B preliminary testing only

Crystal Reports

- Deployed to all training sites
- Integrated into FTD for report development and runtime reports

Integration

Phoenix - CMI

- Integrated into FTD
- Creating Development Manual for local (squadron level) course integration
- Schoolhouse
- New version due in July

Integration Issues

- Have not received preliminary evaluation copies of F/A-18 or H-60
- Possible schedule impact

Support

- Major Trouble assists:
  - NAS JAX
  - NAS North Island
  - NAMTRAGRU MTL development

ASM Development

- All Fleet Beta test events complete (Jan-Mar)
- Updating all NAMTRAGRUDETS to version 1.1
- Currently deploying to 7 squadrons
  - Installed VF2, VF 101, & VFA 106
  - Training VF2

ASM FY00 POA&M

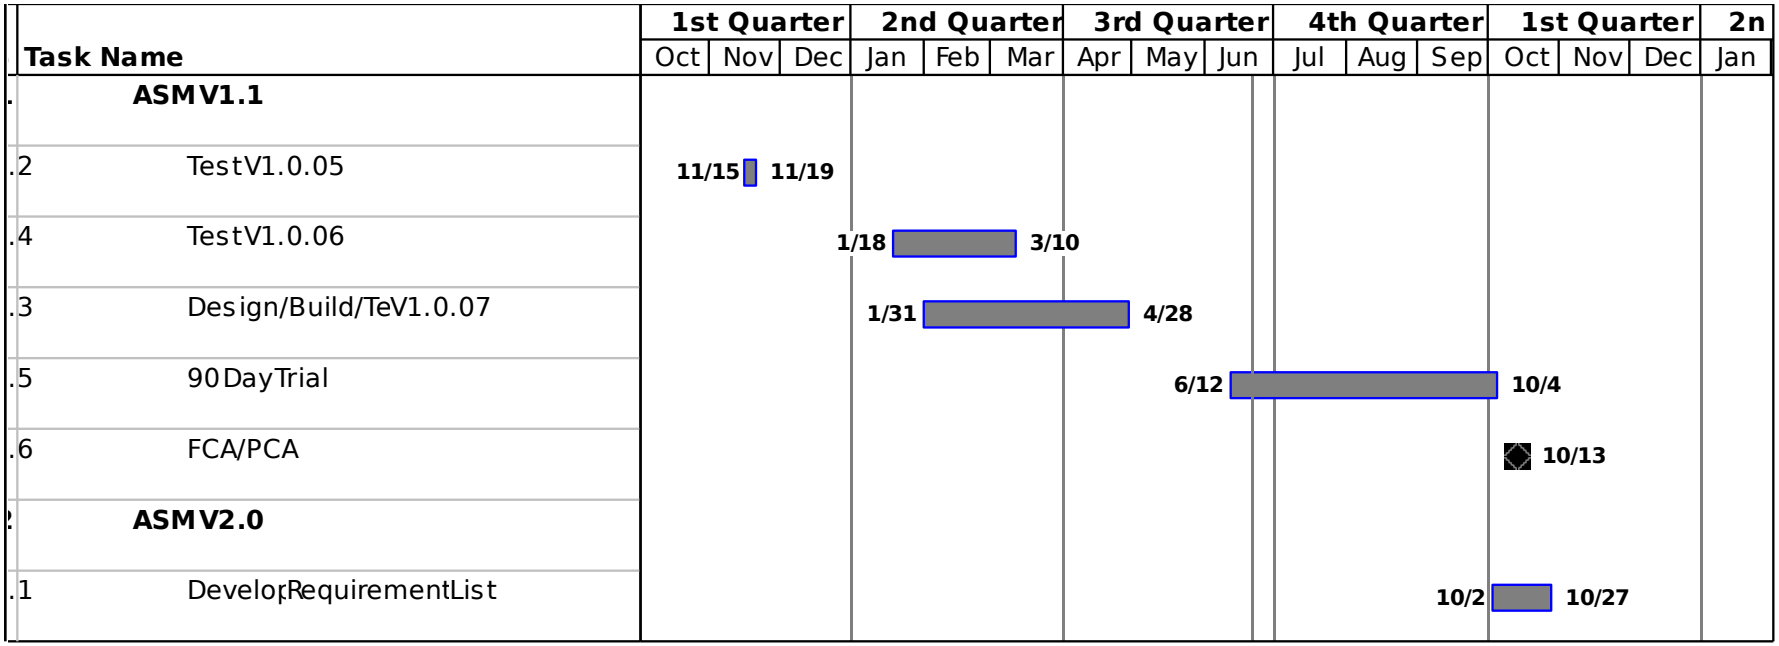

ASM Issues

- F14 ASM
  - Test generation problem
- Reexamining local procedures to explore the addition of further cost effective testing

IPT Action Items

AI-79	Develop and promulgate standardized procedures for loading AMTCS Aviation Support Modules (ASMs) software OR initiate appropriate plans for site by site visits to assist in the installation.	NUWC-Keyport	To be updated at the next IPT meeting	Currently pre-loading ASM for 7 deployments. If networks are installed plan to install ASM. Otherwise, provide ASM on CDs.
AI-85	Recall CBT hardware/software from MCAS Miramar F/A-18 squadron and retain until further notice	NUWC-Keyport	To be updated at the next IPT meeting	KPT has received all hardware available plus DD200 for missing items
AI-93	TYCOMs coordinate establishment of MTL accounts with NUWC Keyport.	TYCOMS/ NUWC Keyport	To be updated at the next IPT meeting	KPT established accounts for all. However, currently not all can access MTL accounts due to TYCOM system firewall restrictions.
AI-94	Prepare a message for OPNAV (N889H) release, establishing and identifying when and what will be in the AMTCS Software Module (ASM) to be delivered to the fleet	N889H/PM A205 /NUWC Keyport	To be updated at the next IPT meeting	KPT input provided to NAVAIR Chief Douse for message drafting and release.

IPT Action Items

AI-97	NUWC Keyport develop a ROM estimate for providing TYCOMs/USMC sufficient RAM to maintain a complete database by Type/Model/Series (including requirements for support of LAN/WAN/other web related interfaces) for each aviation weapon system under TYCOM/USMC cognizance. (Estimate should be provided in time for discussion at the Requisition Requirements Definition meeting to be scheduled in response to Action Item #95.)	NUWC Keyport	To be updated at the next IPT meeting	KPT needs more detailed requirements in order to provide estimate. (NOTE: Engineering to provide Crawford with questions)
AI-102	Follow up to ensure replacement of the F-14 CBT ICW software package that was issued with a missing "graphics" file	PMA2053D NUWC Keyport F-14 Contractor	To be updated at the next IPT meeting	(NOTE: Info was passed to Crawford from Engineering)
AI-105	(NEW Jan 00) Transfer custody of non-ASM hardware that was to be used to support MTIP to CNAP.	NUWC Keyport CNAP	To be updated at the next IPT meeting	Closed. Custody transferred to CNAP.
